


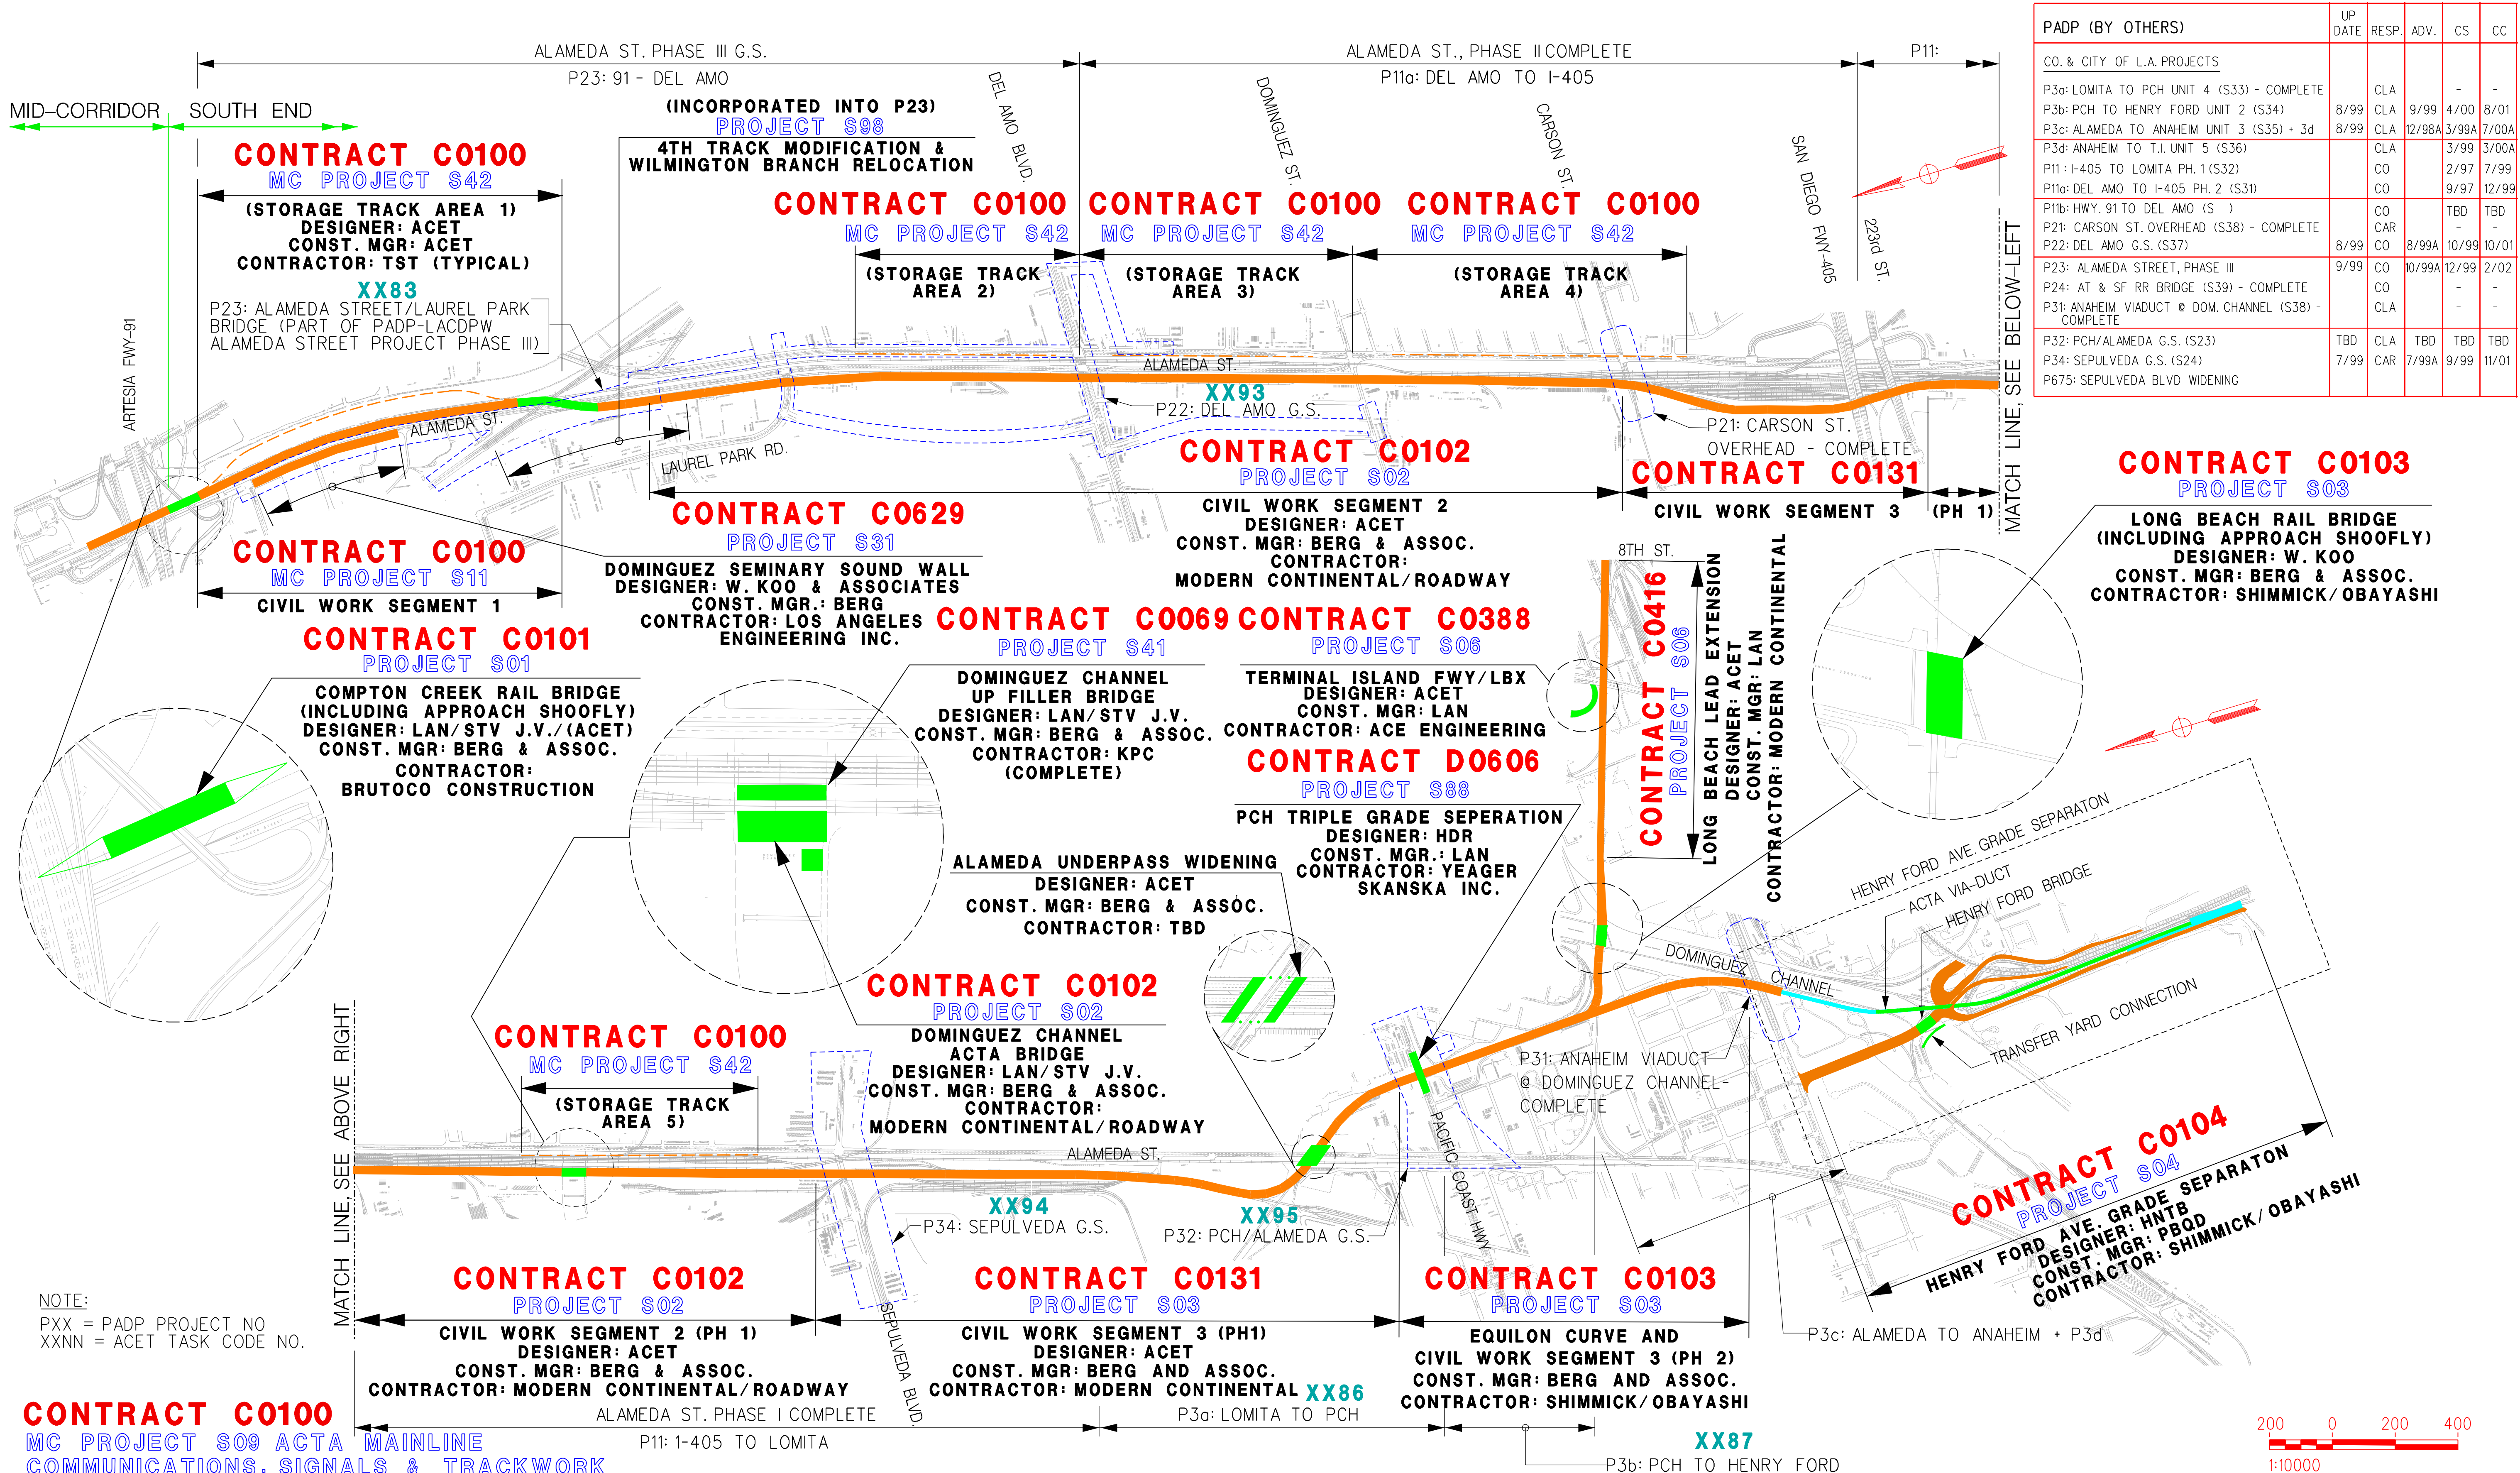

PADP (BY OTHERS)	UP DATE	RESP.	ADV.	CS	CC
CO. & CITY OF L.A. PROJECTS					
P3a: LOMITA TO PCH UNIT 4 (S33) - COMPLETE		CLA		-	-
P3b: PCH TO HENRY FORD UNIT 2 (S34)	8/99	CLA	9/99	4/00	8/01
P3c: ALAMEDA TO ANAHEIM UNIT 3 (S35) + 3d	8/99	CLA	12/98A	3/99A	7/00A
P3d: ANAHEIM TO T.I. UNIT 5 (S36)		CLA		3/99	3/00A
P11: I-405 TO LOMITA PH. 1 (S32)		CO		2/97	7/99
P11a: DEL AMO TO I-405 PH. 2 (S31)		CO		9/97	12/99
P11b: HWY. 91 TO DEL AMO (S)		CO		TBD	TBD
P21: CARSON ST. OVERHEAD (S38) - COMPLETE	8/99	CAR	8/99A	10/99	10/01
P22: DEL AMO G.S. (S37)		CO		-	-
P23: ALAMEDA STREET, PHASE III	9/99	CO	10/99A	12/99	2/02
P24: AT & SF RR BRIDGE (S39) - COMPLETE		CO		-	-
P31: ANAHEIM VIADUCT @ DOM. CHANNEL (S38) - COMPLETE		CLA		-	-
P32: PCH/ALAMEDA G.S. (S23)	TBD	CLA	TBD	TBD	TBD
P34: SEPULVEDA G.S. (S24)	7/99	CAR	7/99A	9/99	11/01
P675: SEPULVEDA BLVD WIDENING					

NOTE:
PXX = PADP PROJECT NO
XXNN = ACET TASK CODE NO.

CONTRACT C0100
MC PROJECT S09 ACTA MAINLINE
COMMUNICATIONS, SIGNALS & TRACKWORK

ALAMEDA CORRIDOR
SOUTH END PROJECTS

PROJECT DEFINITIONS
WITH PADP PROJECTS COORDINATION
